

Project Plan (Final)
WSSOA (IT644) — Autumn 2026

Project Title:

PriceWise – Compare, Analyze, Shop Smarter
A Web-based AI-Powered Smart Shopping Assistant

Date of Submission: 16/08/2026

Submitted By:

Sr. No.	Student Name	Student ID
1	Diya Jain	202512014
2	Tanwani Piyush	202512021
3	Divyesh Dandwani	202512043
4	Harshil Dodwani	202512044
5	Vivek Dhanwani	202512045
6	Yash Gangwani	202512048
7	Aman Rohera	202512049
8	Priya Shah	202512100

Submitted To:

Prof. Jayprakash Lalchandani
Course Instructor – WSSOA (IT644), DAU, Autumn 2026

Note on This Revision

This Project Plan has been corrected and re-aligned with the approved Project Proposal (2.0) and its detailed “Roles and Responsibilities” / “Individual Contribution Detail” sections. The earlier draft assigned some tasks to team members that conflicted with their sole-ownership responsibilities defined in the proposal. The key corrections made are:

- Diya Jain's timeline was rebuilt from scratch. She is the sole owner of Backend Support, API Testing, API Documentation, Integration Testing, Bug Tracking & Verification, Technical Documentation, Final Testing Support, and Report & Presentation — not core backend development, authentication, or deployment, which the earlier draft had incorrectly listed under her name.
- “Recommendations” was removed from Piyush Tanwani's AI/ML lane — the Recommendation Engine (design + implementation) is Yash Gangwani's sole-owned task, not Piyush's.
- “Price Prediction” was removed from Yash Gangwani's lane — the Price Prediction model is Piyush Tanwani's sole-owned task; Yash's AI ownership is limited to the Recommendation Engine and price-drop alert logic.
- The Overall Project Timeline now explicitly includes the Product Identity Matching pipeline and the Price Notification System as Feature Integration tasks, since these are core technical components defined in Proposal 2.0 (Sections 7–9) that were missing from the earlier plan.
- All individual timelines and hour allocations have been re-derived directly from each member's “Individual Contribution Detail” table in the proposal (200 hrs/member, 1,600 hrs total), so effort shown here matches the proposal exactly.

Everything else — the 16-week phase structure, milestone dates, and the Jira-based task management approach — was already consistent with the proposal and has been retained.

Overall Project Timeline

The overall project timeline shows the major tasks and activities planned for the PriceWise project, corrected to match Proposal 2.0. It includes the expected start and end dates of tasks along with important project milestones, and now explicitly reflects the Product Identity Matching pipeline and Price Notification System as part of Feature Integration. This helps the team plan the work and track the progress of different project activities.

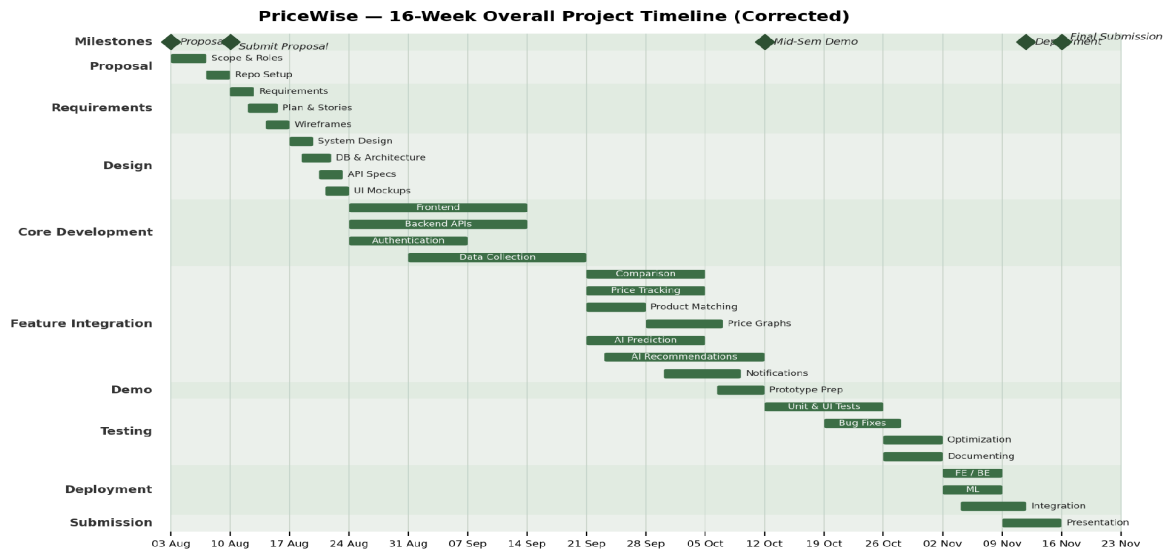


Figure 1.1: Overall Project Timeline and Milestones

Individual Member Timeline

Individual timelines were created to show the tasks assigned to each team member and their planned working period, corrected to match each member's sole-owned tasks as defined in Proposal 2.0's Individual Contribution Detail. These timelines helped in tracking individual progress along with the overall project schedule.

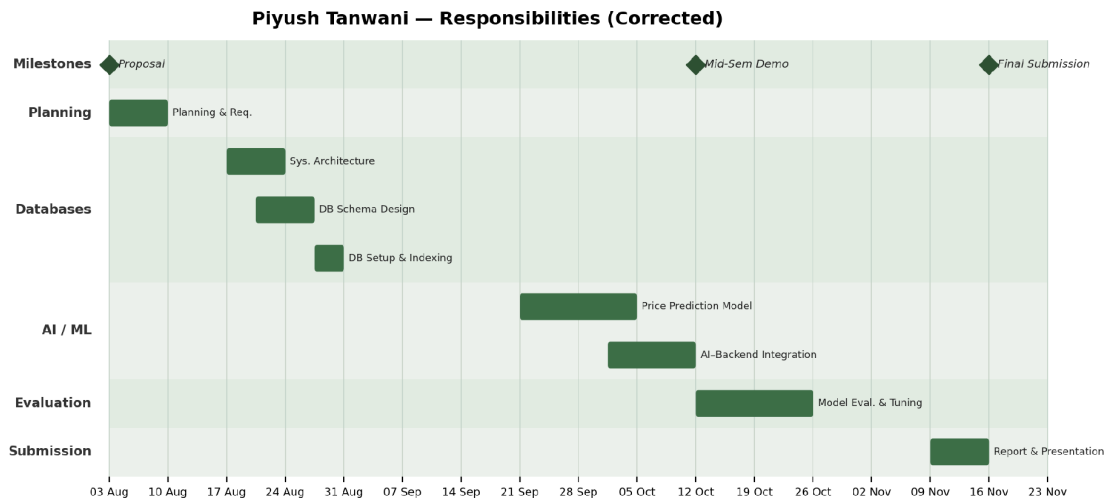


Figure 1.2: Piyush Tanwani — Responsibilities

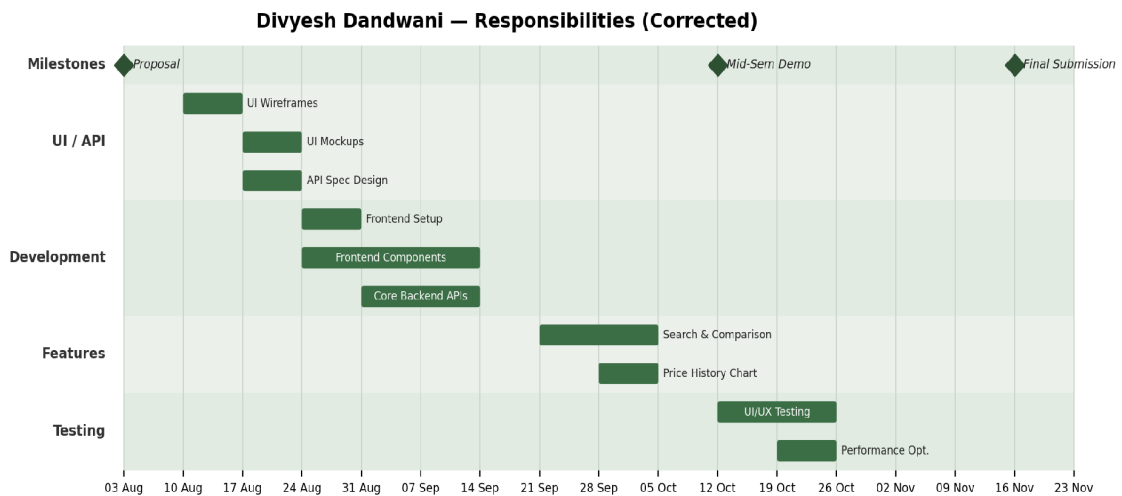


Figure 1.3: Divyesh Dandwani — Responsibilities

DHIRUBHAI AMBANI UNIVERSITY

Diya Jain — Responsibilities (Corrected)

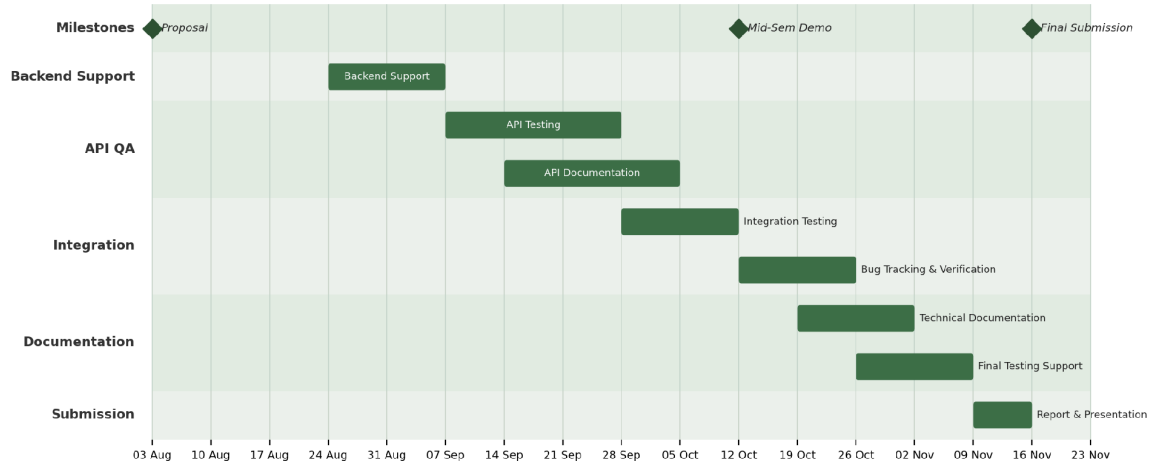


Figure 1.4: Diya Jain — Responsibilities

Vivek Dhanwani — Responsibilities (Corrected)

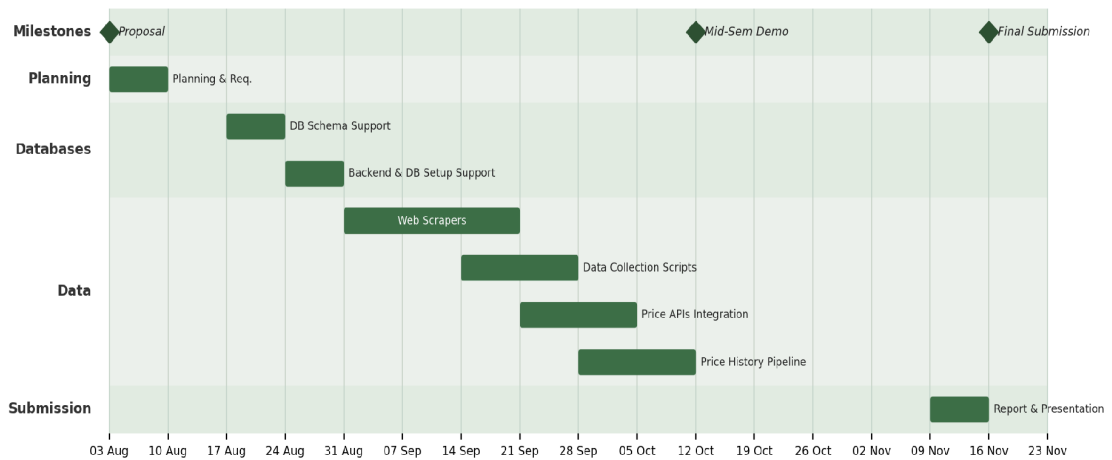


Figure 1.5: Vivek Dhanwani — Responsibilities

DHIRUBHAI AMBANI UNIVERSITY

Yash Gangwani — Responsibilities (Corrected)

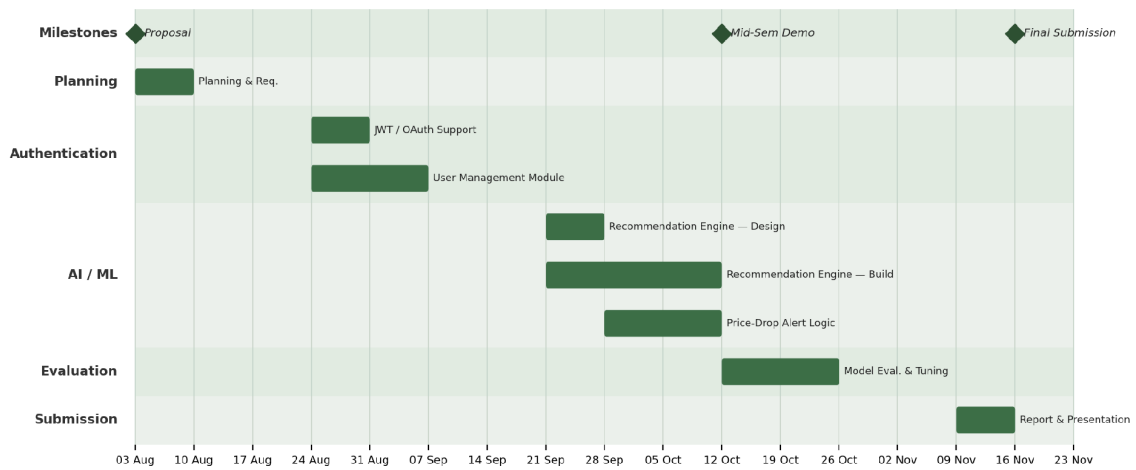


Figure 1.6: Yash Gangwani — Responsibilities

Aman Rohera — Responsibilities (Corrected)

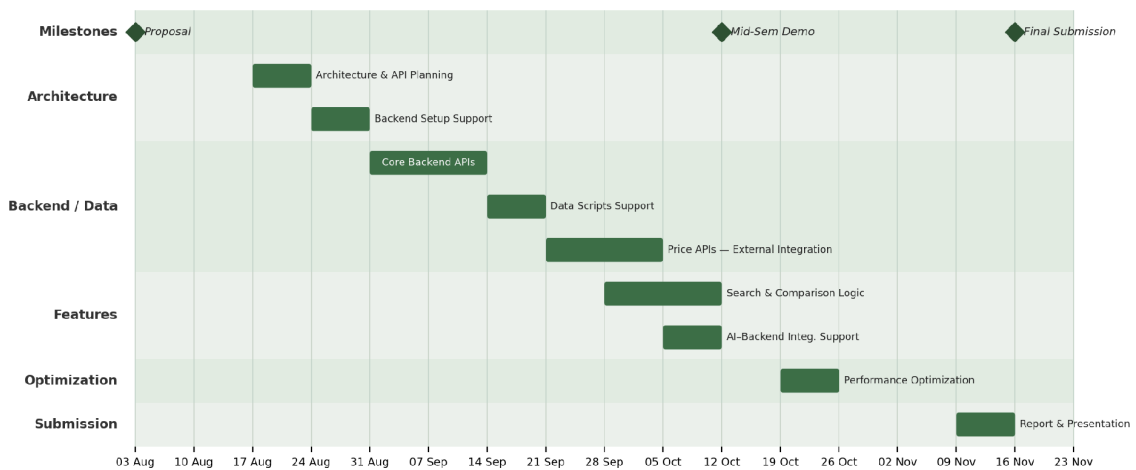


Figure 1.7: Aman Rohera — Responsibilities

DHIRUBHAI AMBANI UNIVERSITY

Harshil Dodwani — Responsibilities (Corrected)

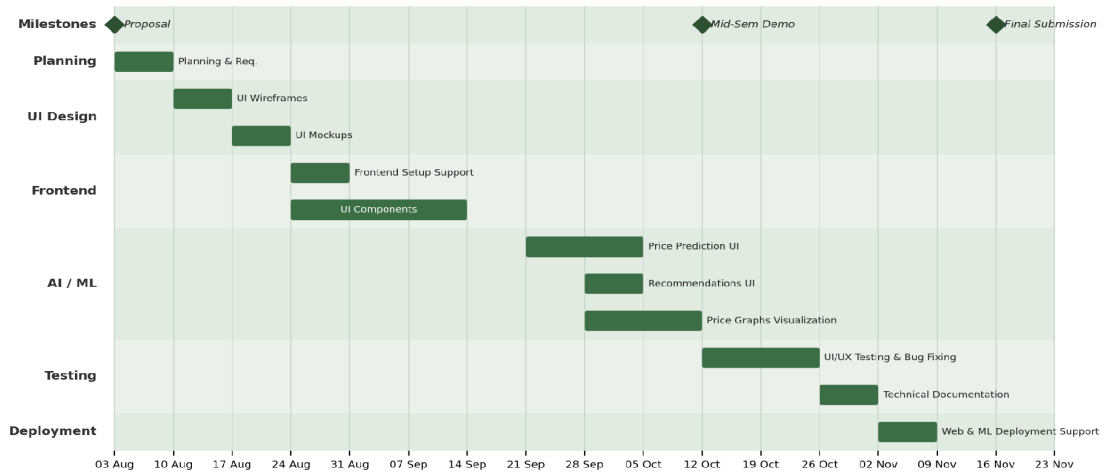


Figure 1.8: Harshil Dodwani — Responsibilities

Priya Shah — Responsibilities (Corrected)

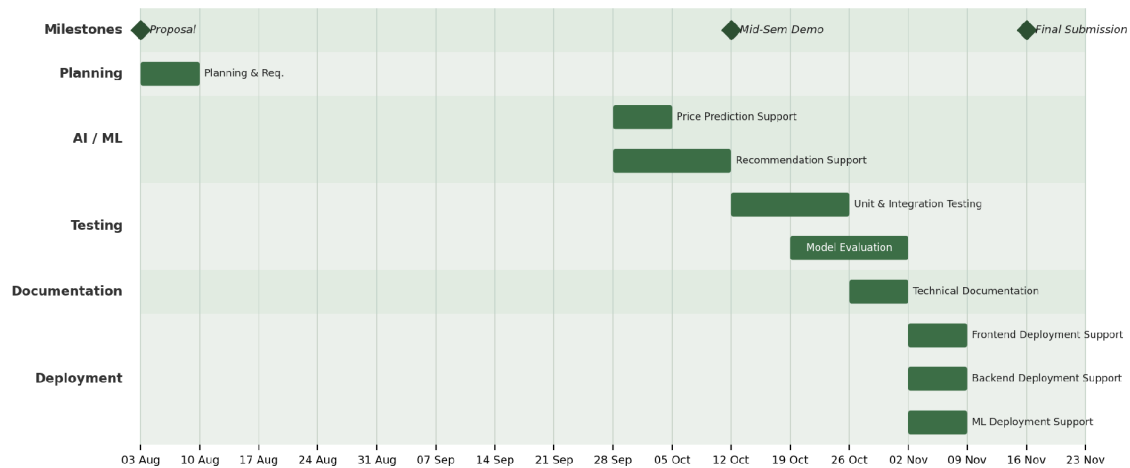


Figure 1.9: Priya Shah — Responsibilities

Team Task Assignments

Each team member is the sole owner of a specific set of tasks, so accountability for every deliverable is unambiguous. Planned effort is approximately 200 hours per member across the 16-week project ($\approx$ 12–13 hrs/week), consistent with Proposal 2.0's Roles and Responsibilities section.

Member	Primary Role	Key Owned Tasks	Effort
Piyush Tanwani	AI/ML Engineer & Database Architect	System architecture design; database schema design & setup; Price Prediction model (Prophet/XGBoost); AI–Backend integration; model evaluation & tuning	200 hrs
Divyesh Dandwani	Frontend Lead & Backend API Integrator	UI wireframes & mockups; API specification design; frontend build; core backend APIs; search & comparison feature; price history chart integration; UI/UX testing & performance optimization	200 hrs
Diya Jain	Backend Support, API Testing & Documentation	Backend support for assigned modules; API testing (Postman/Swagger); API & technical documentation; integration testing; bug tracking & verification; final testing support	200 hrs
Vivek Dhanwani	Data Engineer & Database Support	Database schema support; compliant web scrapers (Croma etc.); data collection scripts; Flipkart/Amazon price API integration; price-history pipeline	200 hrs
Yash Gangwani	Authentication & Recommendation Engine Developer	JWT/OAuth support; User Management module; Recommendation Engine design & implementation (Scikit-learn); price-drop alert logic; model evaluation & tuning	200 hrs
Aman Rohera	Backend & External API Integration Specialist	External API integration contracts; core backend offer-aggregation APIs; Flipkart Affiliate API & Amazon PA-API clients; search & comparison ranking logic; API performance optimization	200 hrs
Harshil Dodwani	UI/UX Designer & Frontend–AI Integration	UX requirements & wireframes; design system components; Price Prediction UI; Recommendations UI; price-trend graph visualization; UI/UX testing; deployment support	200 hrs
Priya Shah	QA Lead & AI Model Testing	Test-plan & acceptance criteria; platform-wide unit & integration testing; ML model accuracy/precision evaluation; QA documentation; pre-release deployment verification	200 hrs
Total	8 members		1,600 hrs

Project Timeline and Task Management

Jira is used for managing and tracking the tasks of the PriceWise project. It helps the team divide the project into different tasks, assign them to team members, set timelines, and track the progress of the work.

Project Management Tool Used: Jira

The main activities managed through Jira are:

- Creating and assigning tasks
- Setting task deadlines
- Tracking task progress
- Managing project milestones
- Maintaining the overall project timeline

The Jira workspace is organised as a single “PriceWise” team with sub-teams for AI & ML, Data & Scraping, Backend & API, QA & Deployment, and Frontend & UI, with Epics for each project phase (Project Planning & Design, Core Development, Feature Integration & AI, Testing & Refinement, Deployment & Final Delivery), a Kanban board, sprint backlog, and calendar view for task scheduling — as shown in the team's live Jira workspace.
